











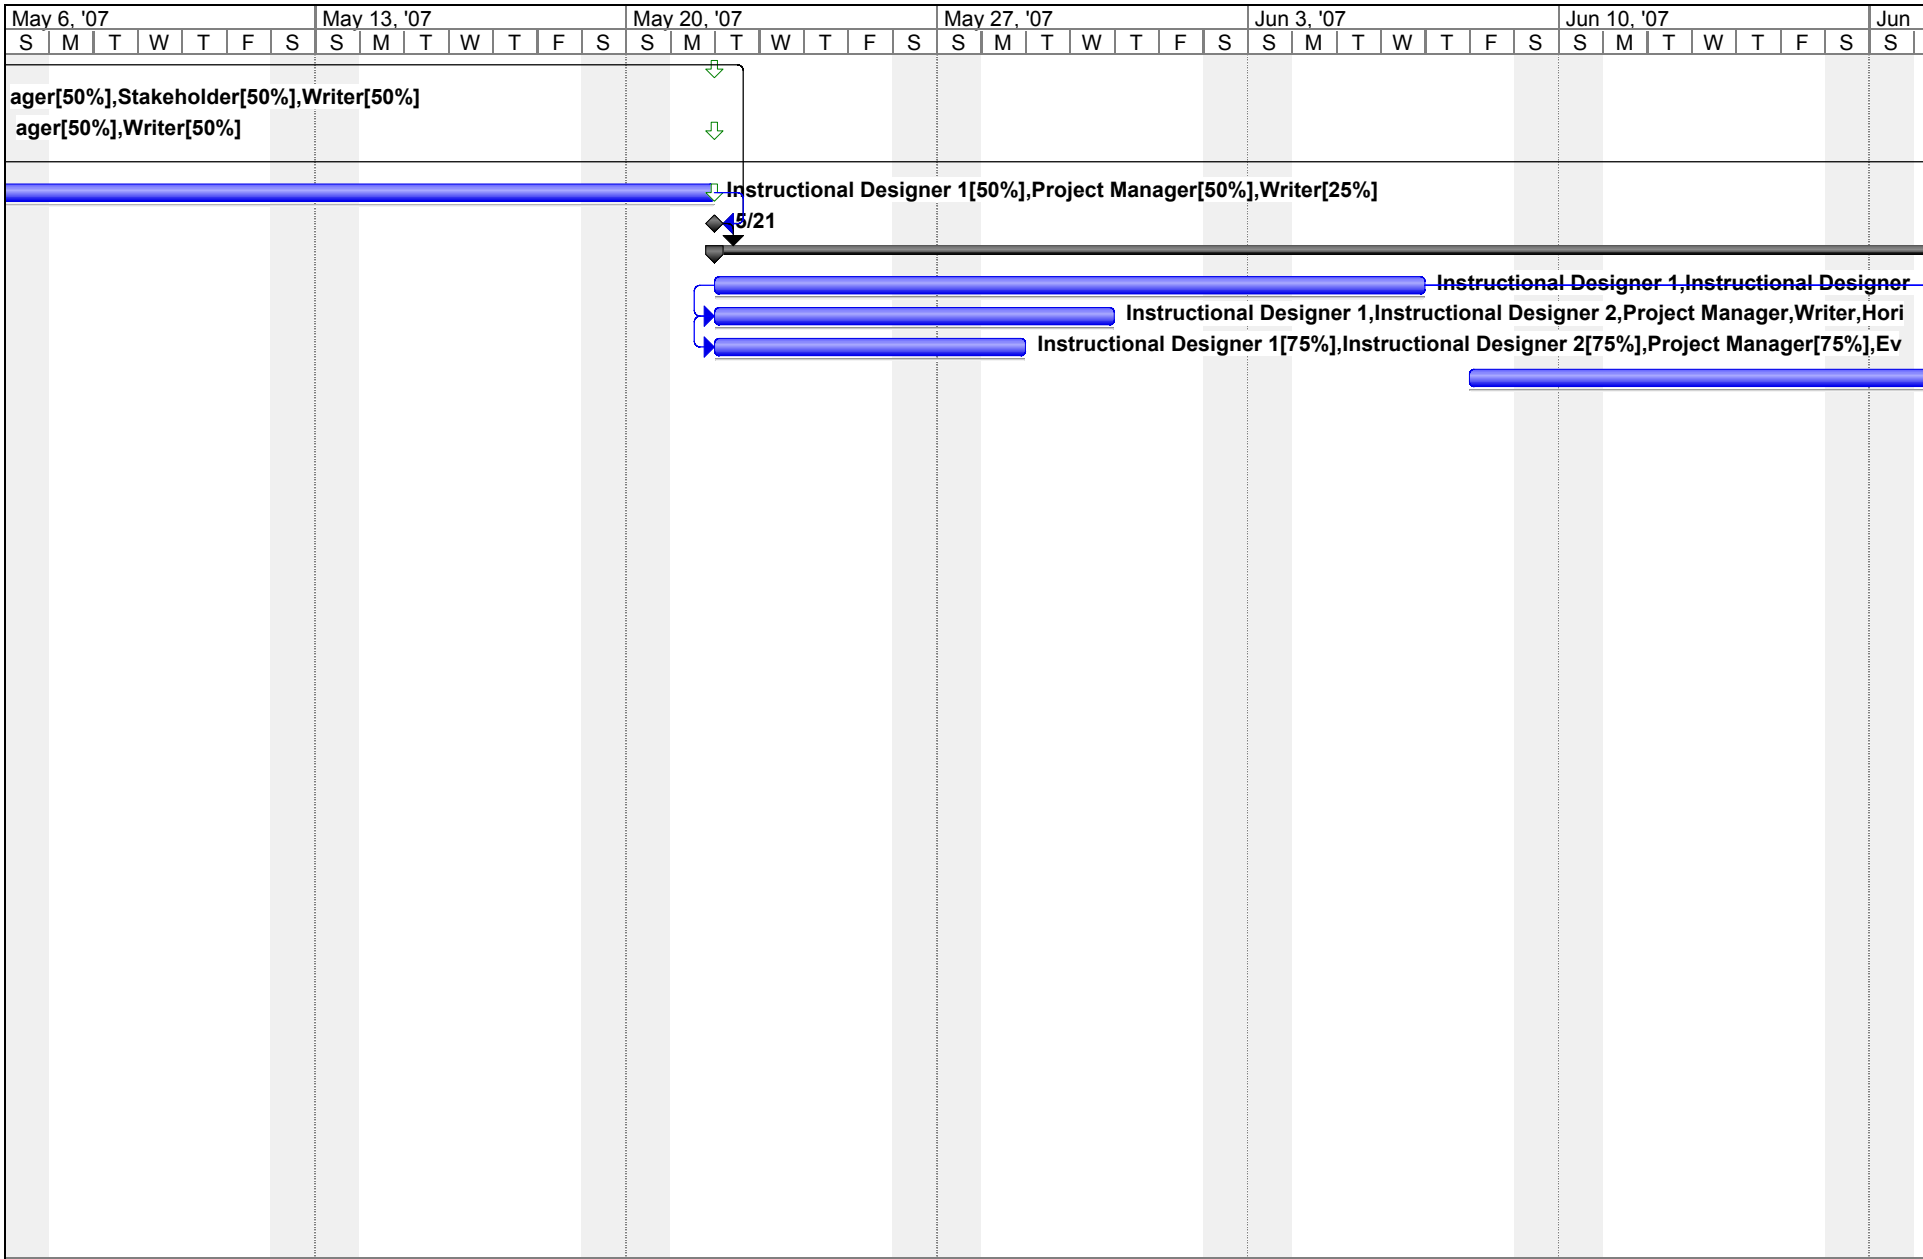
ID	Task Name	Duration	Start	Finish	Predecessors	7							Apr 22, '07							Apr 29, '07						
						T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		
1	Plan	6 days?	Wed 4/18/07	Wed 4/25/07																						
2	Planning Meeting	1 day?	Wed 4/18/07	Wed 4/18/07																						
3	Draft Development Plan	6 days	Wed 4/18/07	Wed 4/25/07	2SS																					
4	Approve Development Plan	0 days	Wed 4/18/07	Wed 4/18/07	2FF,3SS																					
5	Draft Goals	17 days	Fri 4/27/07	Mon 5/21/07																						
6	Approve Goals	0 days	Mon 5/21/07	Mon 5/21/07	5FF,1FF																					
7	Project Design	37 days	Tue 5/22/07	Wed 7/11/07	6																					
8	Task Analysis	12 days	Tue 5/22/07	Wed 6/6/07																						
9	Set Course Objectives	7 days	Tue 5/22/07	Wed 5/30/07	8SS																					
10	Assessment Strategies	5 days	Tue 5/22/07	Mon 5/28/07	9SS																					
11	Content Development	24 days	Fri 6/8/07	Wed 7/11/07																						
12	Approve Objectives	0 days	Tue 7/17/07	Tue 7/17/07	11,7FF																					
13	Project Development Plannin	6 days	Wed 7/18/07	Wed 7/25/07	7,12																					
14	Delineate Project Task	2 days	Wed 7/18/07	Thu 7/19/07																						
15	Develop a Projected Workl	3 days	Wed 7/18/07	Fri 7/20/07	14SS																					
16	Develop a Project Schemul	4 days	Fri 7/20/07	Wed 7/25/07																						
17	Create Course Shell and Sectio	0 days	Thu 7/26/07	Thu 7/26/07	13FF																					
18	Content Development	45 days	Tue 7/31/07	Mon 10/1/07	17																					
19	Instructional Strategies	16 days	Tue 7/31/07	Tue 8/21/07	8FF																					
20	Learning Activities	10 days	Mon 8/6/07	Fri 8/17/07	8FF,19FF																					
21	Assessment Items	15 days	Mon 8/13/07	Fri 8/31/07	20FF																					
22	Content	15 days	Mon 8/13/07	Fri 8/31/07	19SS,21FF																					
23	Approval For Content Plan	0 days	Fri 8/31/07	Fri 8/31/07	22FF																					
24	Develop Instructor Guide	21 days	Mon 9/3/07	Mon 10/1/07																						
25	Draft Date	21 days	Mon 9/3/07	Mon 10/1/07																						
26	Approved	0 days	Mon 10/1/07	Mon 10/1/07	25FF																					
27	Develop Student Guide/D	21 days	Mon 9/3/07	Mon 10/1/07	24SS																					
28	Draft Date	21 days	Mon 9/3/07	Mon 10/1/07	25SS,4FF,26FF																					
29	Approved	0 days	Mon 10/1/07	Mon 10/1/07	26SS,28FF																					
30	Assessment Development	5 days	Tue 9/25/07	Mon 10/1/07	29FF																					
31	Develop Instructional Mate	35 days	Tue 8/14/07	Mon 10/1/07	22SS,30FF																					
32	Assessment Approved	0 days	Mon 10/1/07	Mon 10/1/07	30,18FF,31FF																					
33	Formative Evaluation	5 days	Tue 10/2/07	Mon 10/8/07	32SS																					
34	Instructional materials	5 days	Tue 10/2/07	Mon 10/8/07																						
35	Student Course	5 days	Tue 10/2/07	Mon 10/8/07																						
36	Instructor Course	5 days	Tue 10/2/07	Mon 10/8/07	35FF																					
37	Assessment Materials	5 days	Tue 10/2/07	Mon 10/8/07	34SS,36FF																					
38	Awareness Materials Draft	20 days	Tue 10/9/07	Mon 11/5/07																						
39	Awareness Materials Approved	0 days	Mon 11/5/07	Mon 11/5/07	38FF,33																					












Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	7							Apr 22, '07							Apr 29, '07						
						T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		
40	Test Run Course (Formative I	9 days	Tue 11/6/07	Fri 11/16/07	39																					
41	One-to-one Evaluation	9 days	Tue 11/6/07	Fri 11/16/07																						
42	Small Group Evaluation	9 days	Tue 11/6/07	Fri 11/16/07	41SS																					
43	Train the Trainers (Implementat	2 days	Mon 11/19/07	Tue 11/20/07	40																					
44	Formative Evaluation/Data Fror	9 days	Mon 11/19/07	Thu 11/29/07	43SS																					
45	Final Training Date	1 day	Fri 11/30/07	Fri 11/30/07	44																					
46	Summative Evaluation	95 days	Fri 12/7/07	Thu 4/17/08	45																					
47	Summative Report Written	6 days	Fri 4/18/08	Fri 4/25/08	46																					
48	Summative Report Review	4 days	Mon 4/28/08	Thu 5/1/08	47																					

Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

May 6, '07							May 13, '07							May 20, '07							May 27, '07							Jun 3, '07							Jun 10, '07							Jun
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S



Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

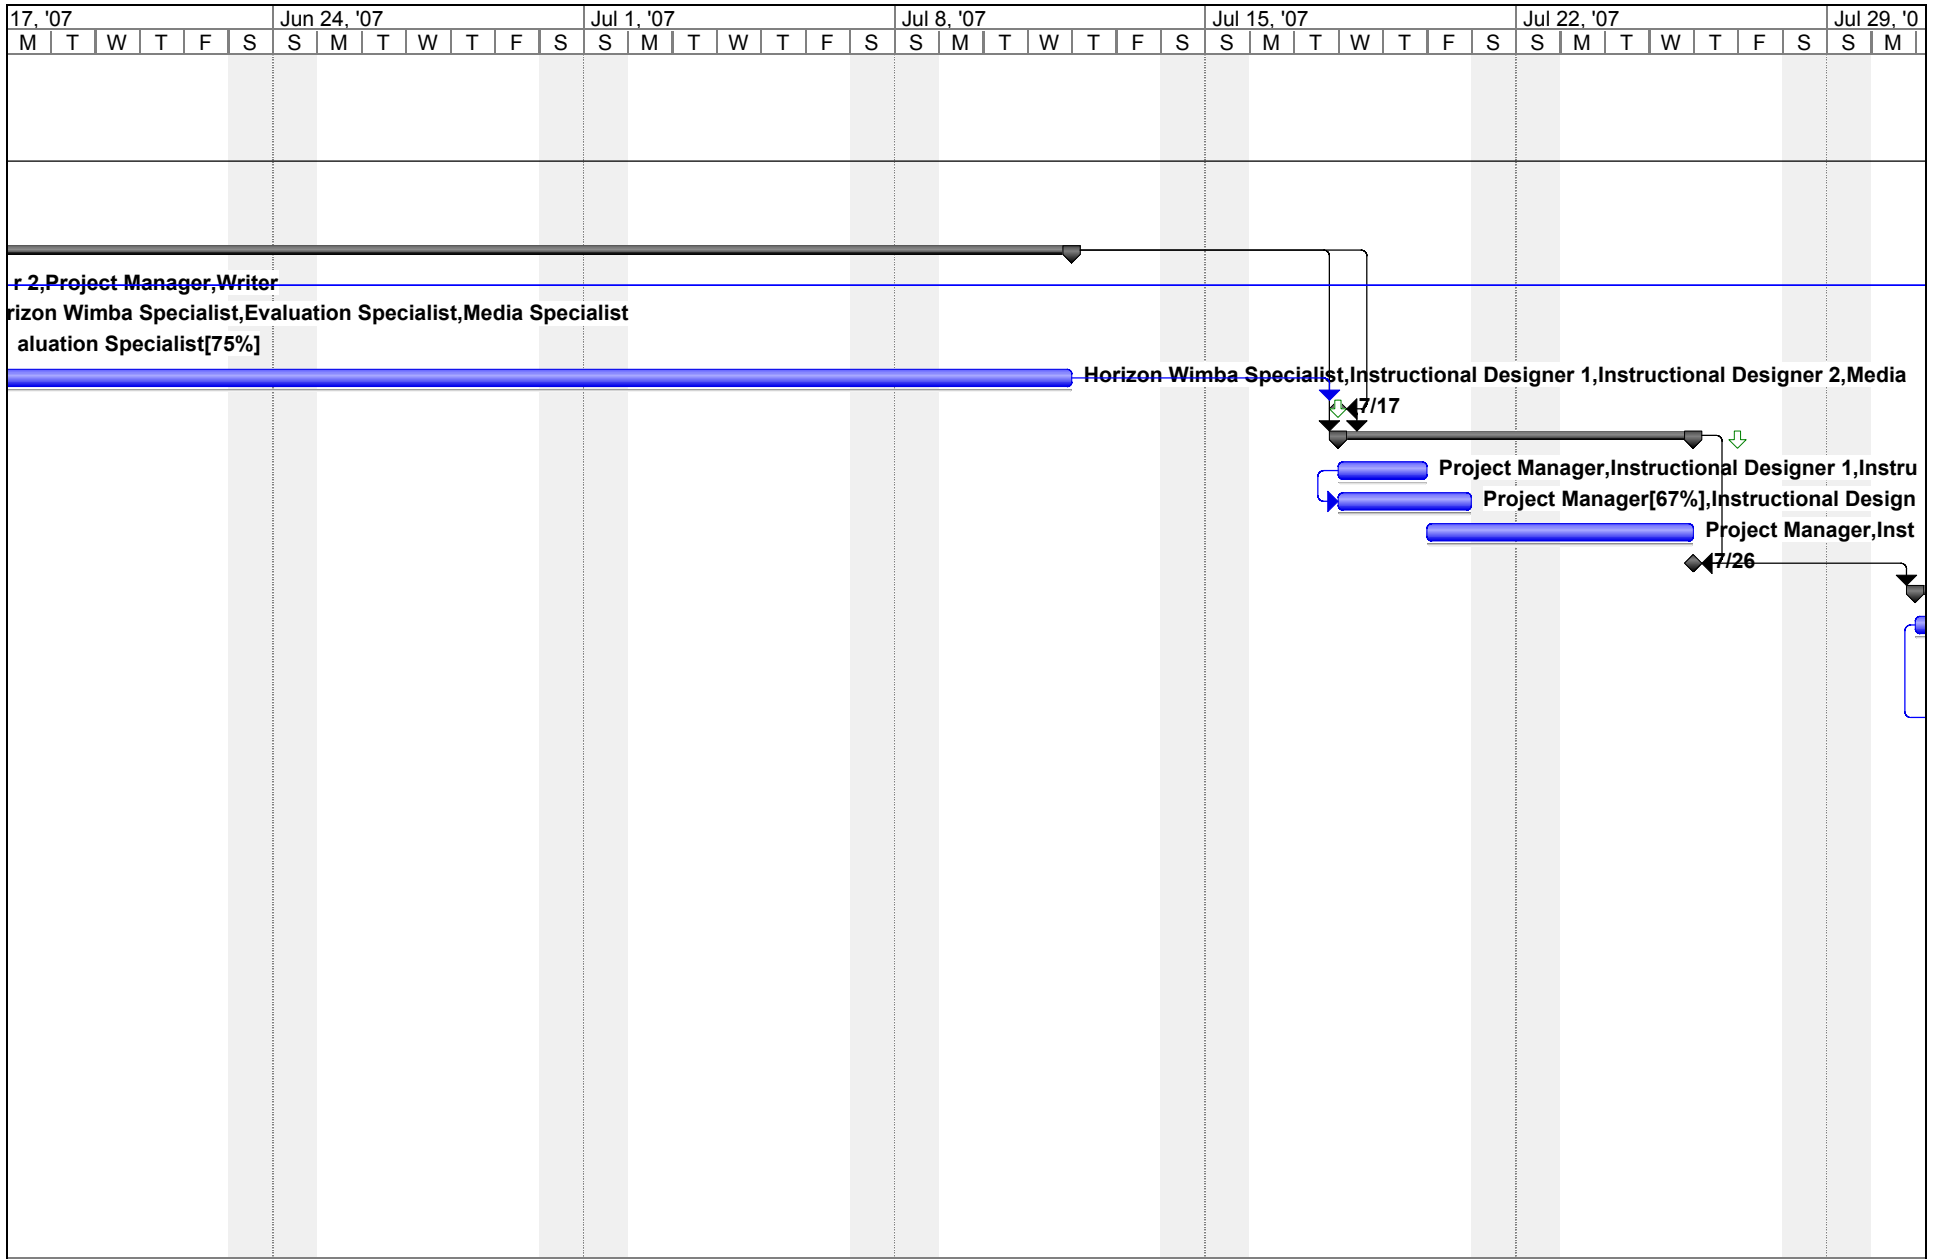










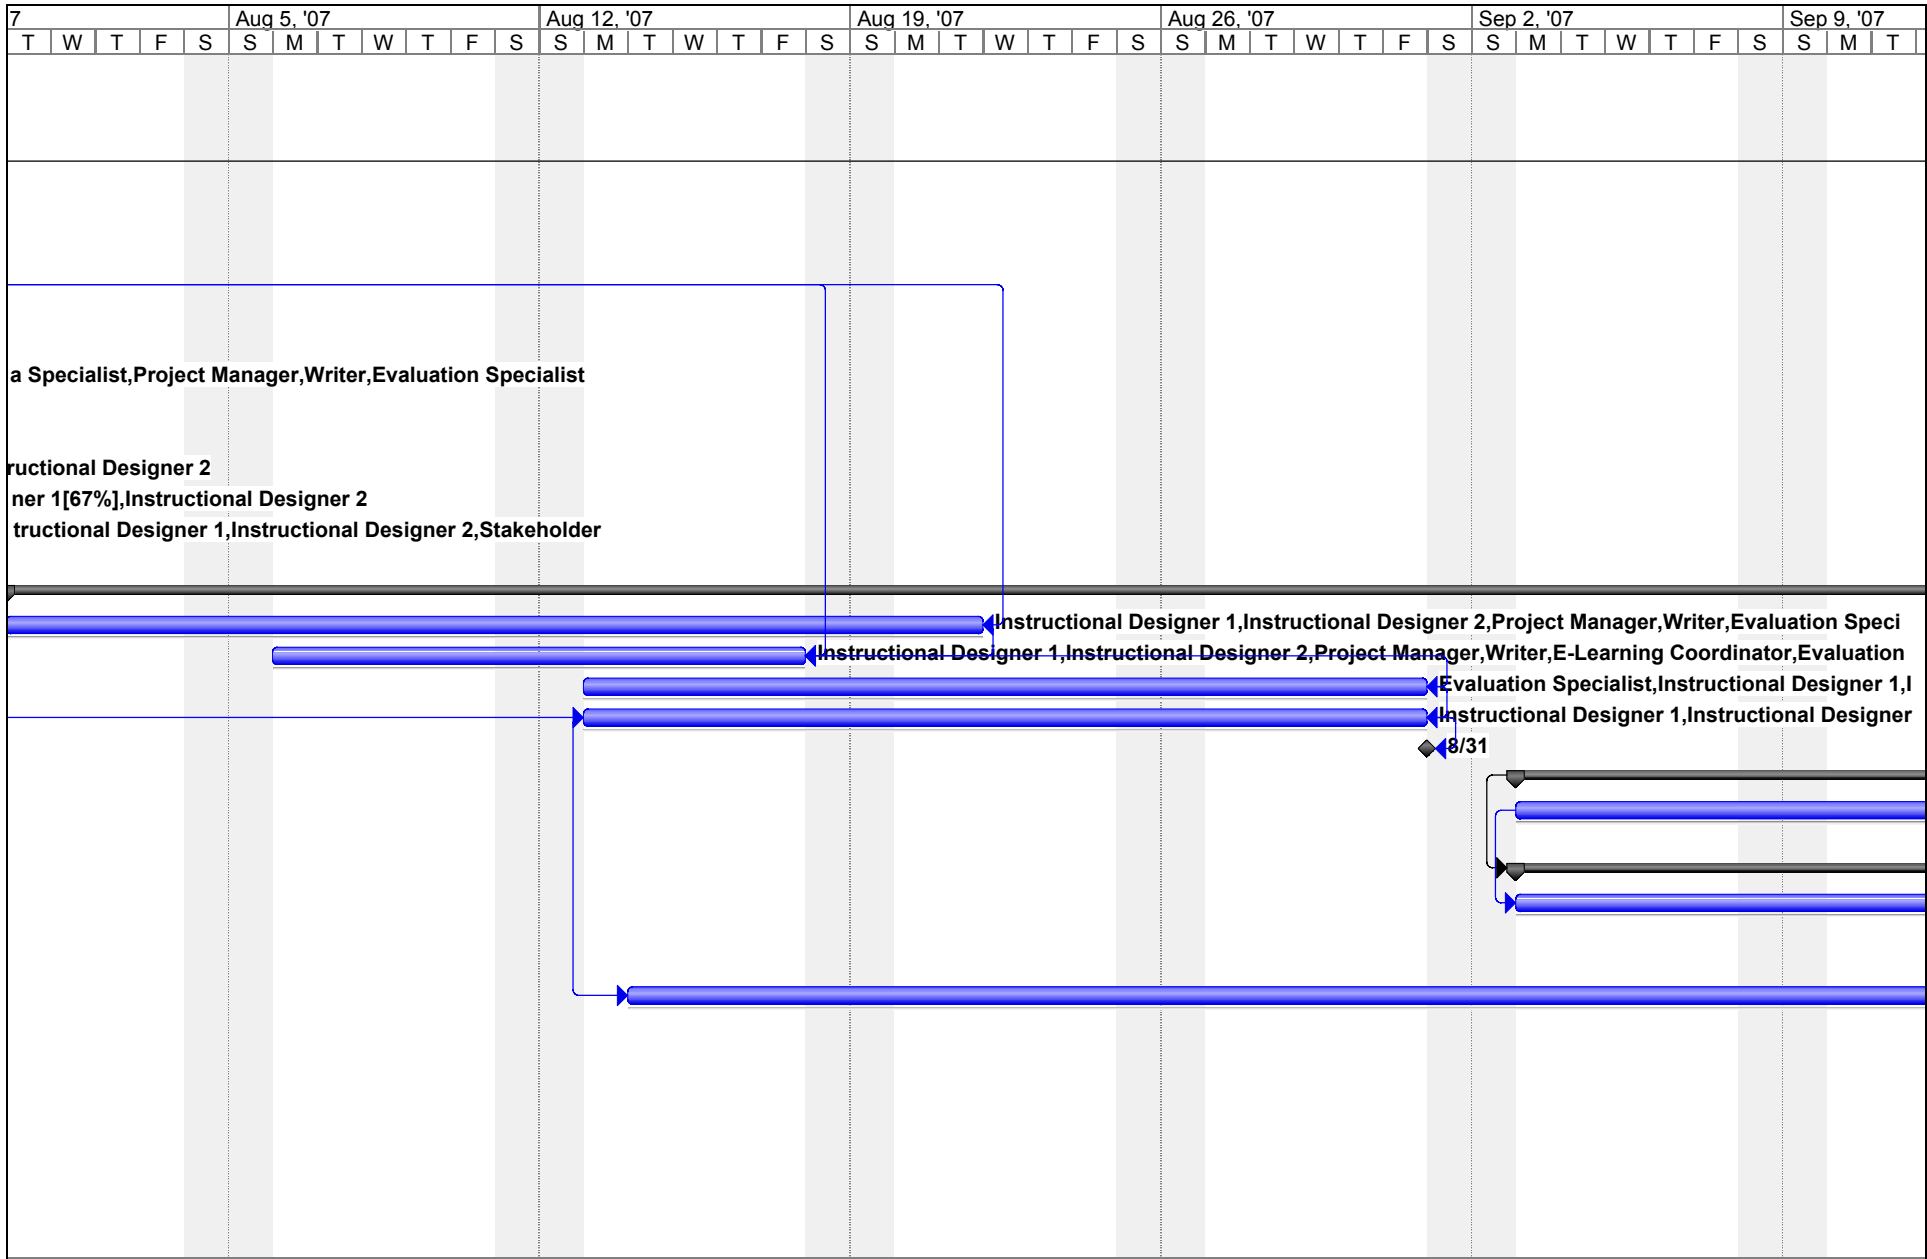
Project: Wimba Project Proposal 3
 Date: Sat 5/5/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

17, '07						Jun 24, '07						Jul 1, '07						Jul 8, '07						Jul 15, '07						Jul 22, '07						Jul 29, '0						
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M



Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 












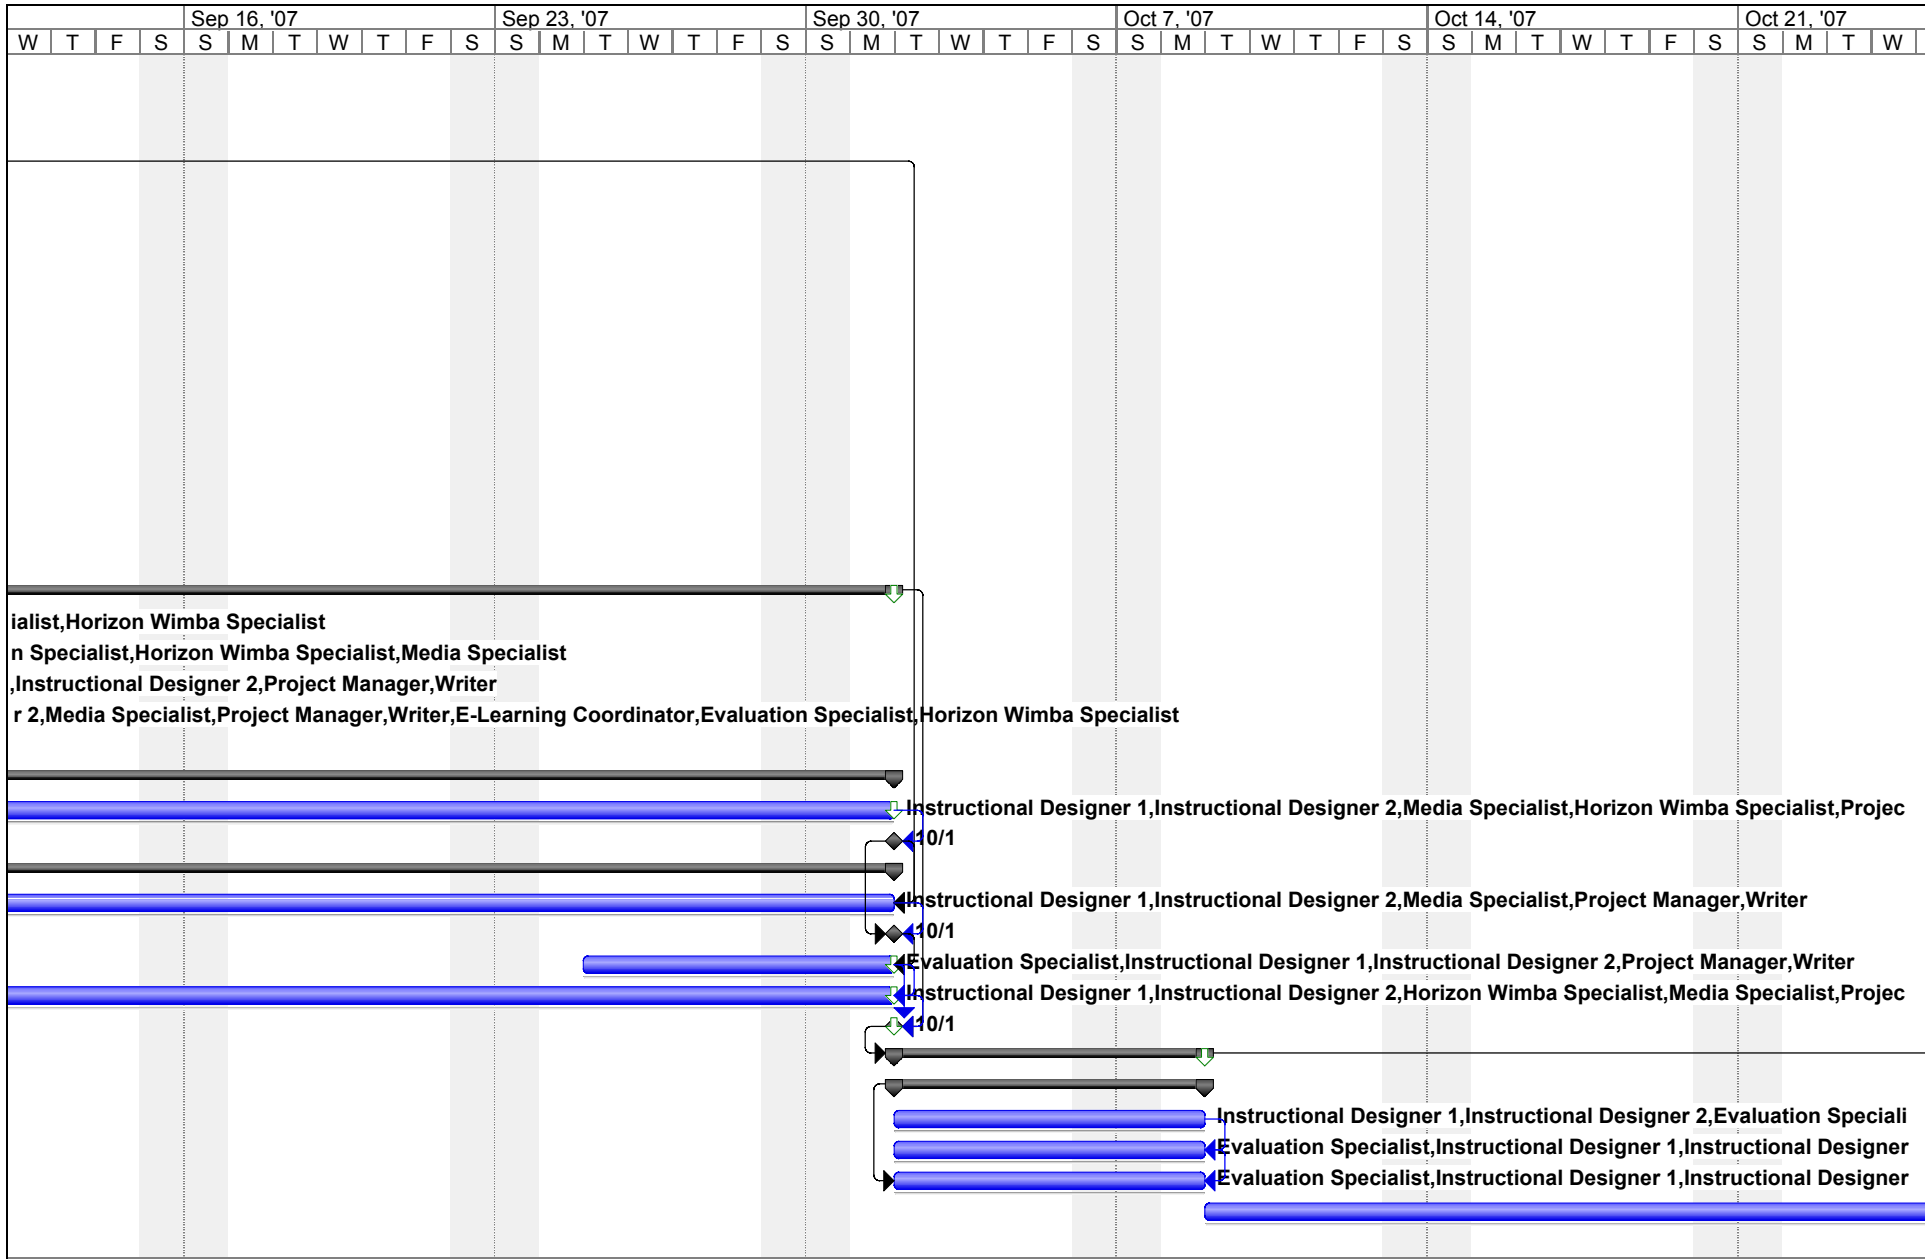
Project: Wimba Project Proposal 3
Date: Sat 5/5/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

7					Aug 5, '07					Aug 12, '07					Aug 19, '07					Aug 26, '07					Sep 2, '07					Sep 9, '07					
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T



Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	












Project: Wimba Project Proposal 3
Date: Sat 5/5/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	


				Sep 16, '07				Sep 23, '07				Sep 30, '07				Oct 7, '07				Oct 14, '07				Oct 21, '07															
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W				



Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 





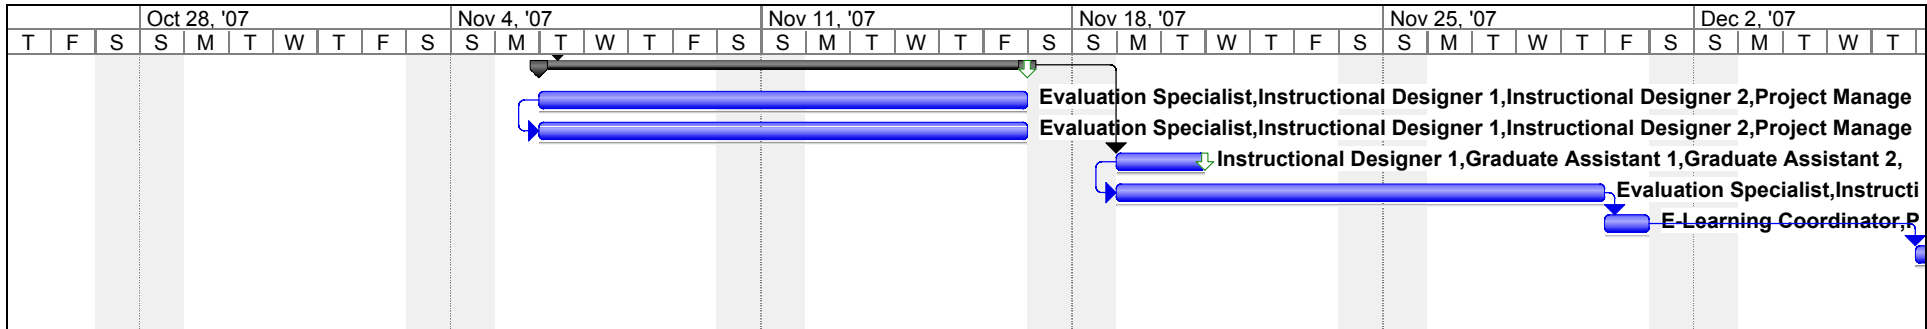






Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Wimba Project Proposal 3
 Date: Sat 5/5/07










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

		Dec 9, '07							Dec 16, '07							Dec 23, '07							Dec 30, '07							Jan 6, '08							Jan 13, '08													
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S							










Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

		Dec 9, '07							Dec 16, '07							Dec 23, '07							Dec 30, '07							Jan 6, '08							Jan 13, '08						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
er,E-Learning Coordinator,Server Administrator er,E-Learning Coordinator,Server Administrator ,E-Learning Coordinator,Project Manager,Server Administrator tional Designer 1,Instructional Designer 2,Project Manager Project Manager																																											



Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


Jan 20, '08							Jan 27, '08							Feb 3, '08							Feb 10, '08							Feb 17, '08							Feb 24, '08							
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S







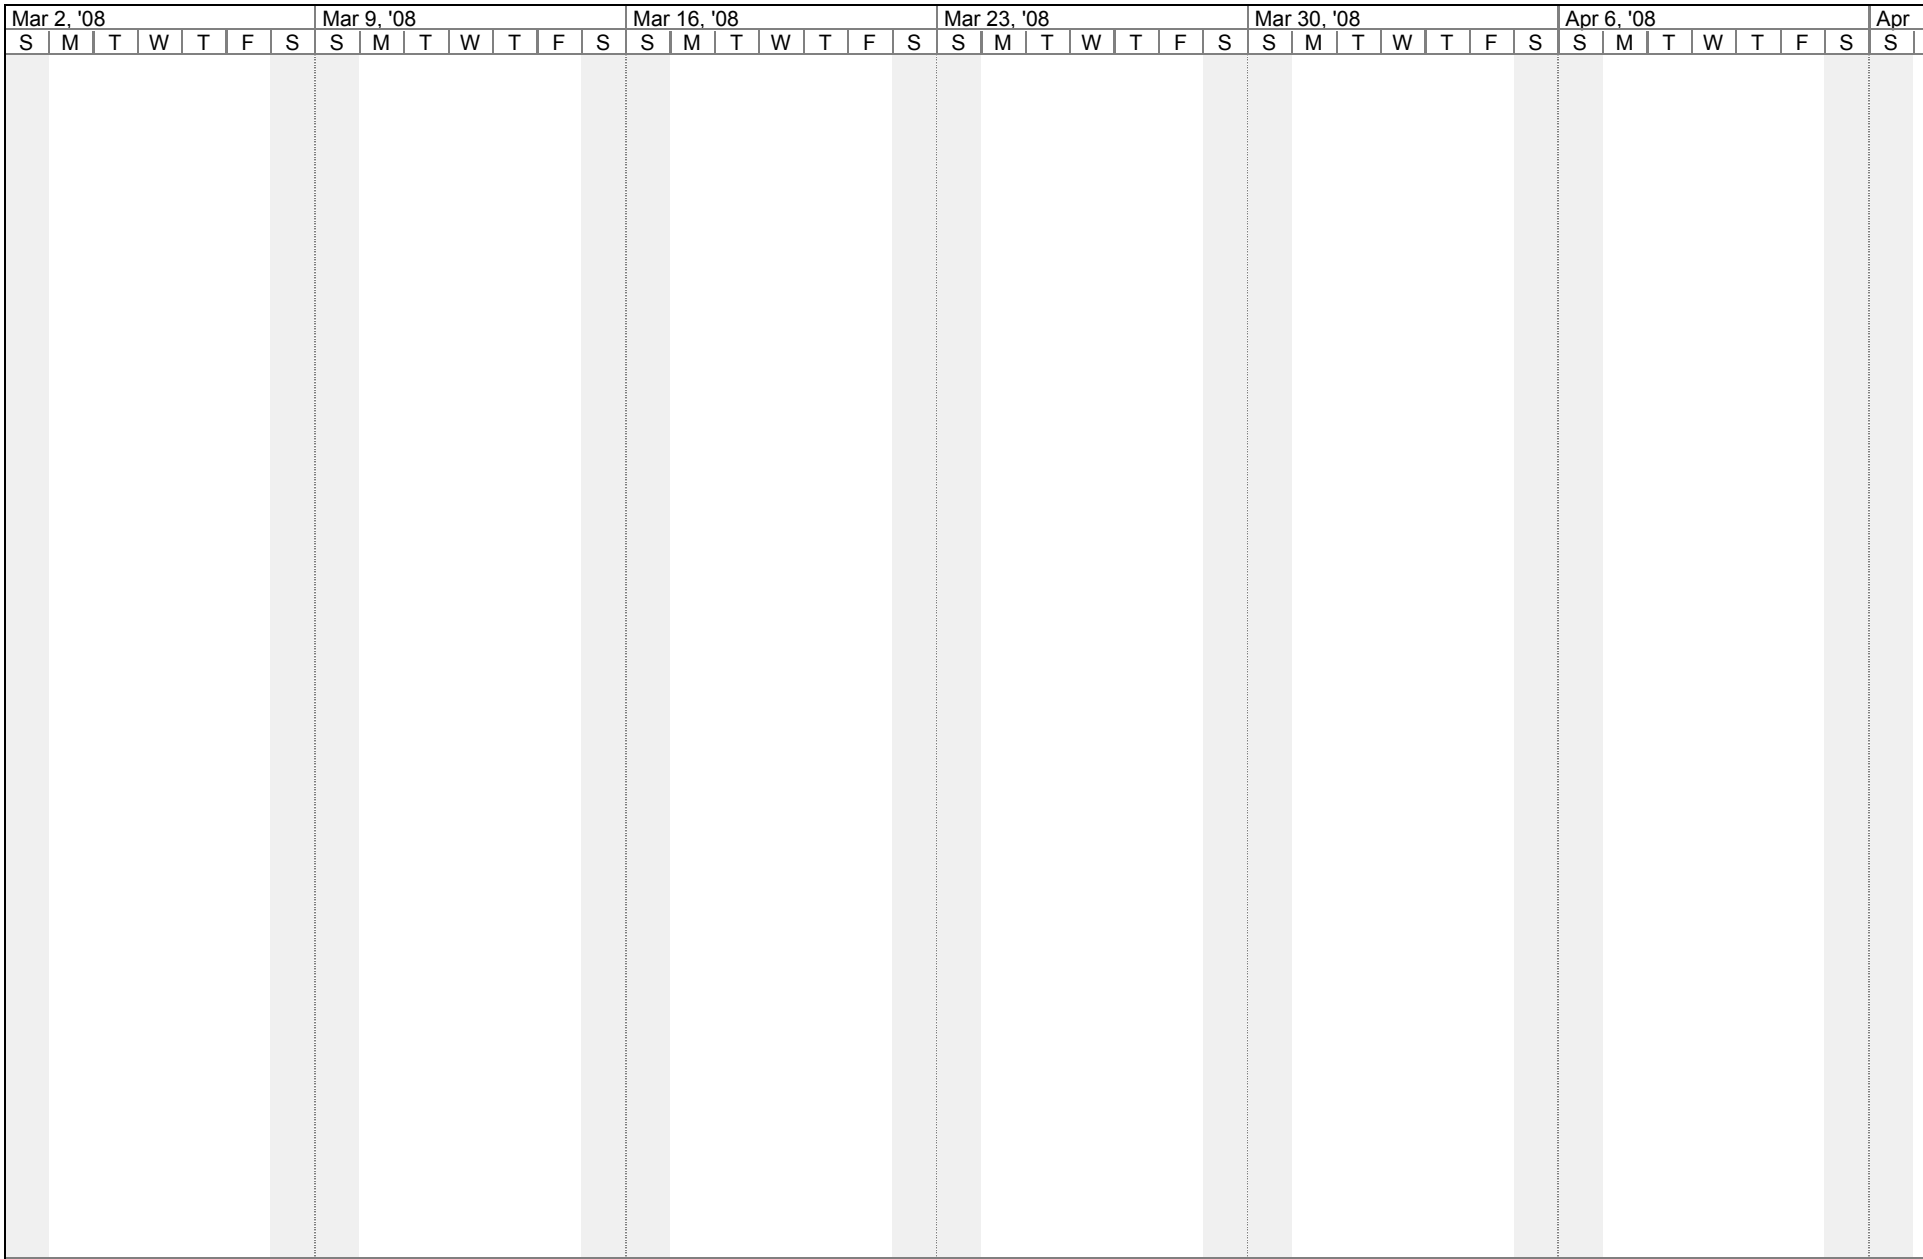


Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 

Jan 20, '08							Jan 27, '08							Feb 3, '08							Feb 10, '08							Feb 17, '08							Feb 24, '08							
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S



Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Mar 2, '08							Mar 9, '08							Mar 16, '08							Mar 23, '08							Mar 30, '08							Apr 6, '08							Apr
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S

Project: Wimba Project Proposal 3
Date: Sat 5/5/07



Milestone



Summary



Project Summary



External Tasks



External Milestone




Deadline





Project: Wimba Project Proposal 3 Date: Sat 5/5/07	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

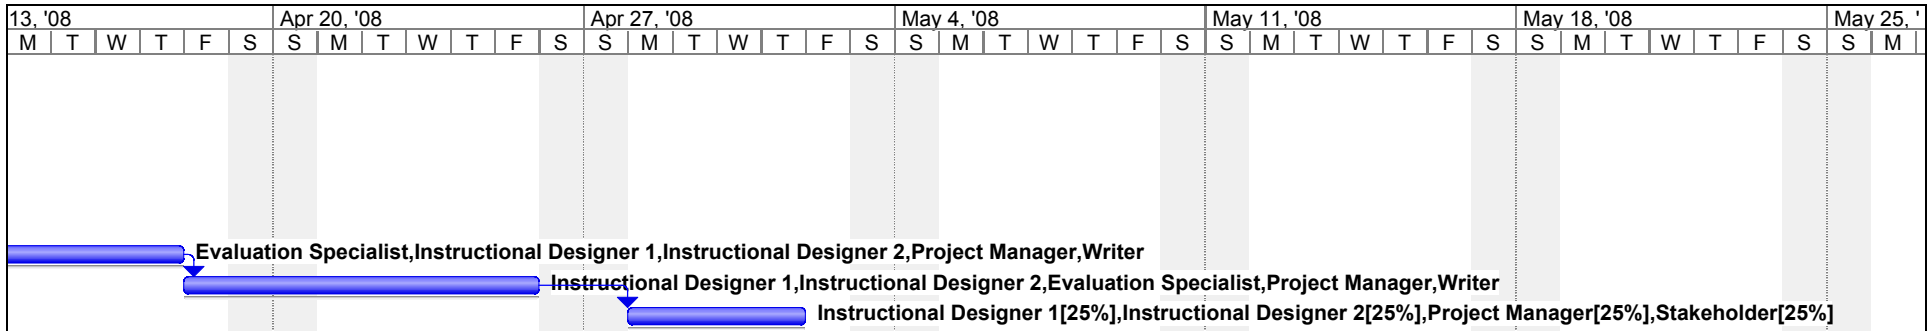

Project: Wimba Project Proposal 3
Date: Sat 5/5/07

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
