










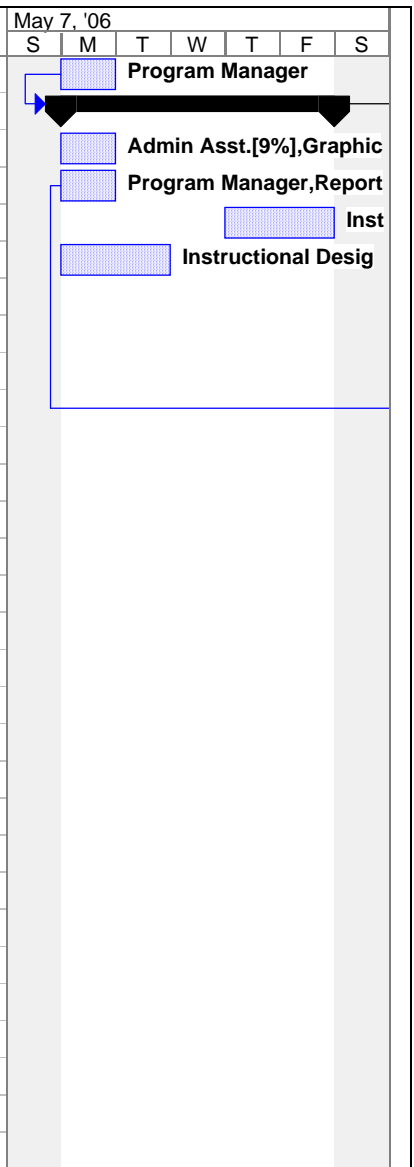




ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	May 7, '06						
							S	M	T	W	T	F	S
1	Start Project	1 day	Mon 5/8/06	Mon 5/8/06		Program Manager							
2	Plan Project	5 days	Mon 5/8/06	Fri 5/12/06	1SS								
3	Planning Meeting	1 day	Mon 5/8/06	Mon 5/8/06		Admin Asst.[9%],Graphic A							
4	Prepare Objectives	1 day	Mon 5/8/06	Mon 5/8/06		Program Manager,Reports							
5	Conduct content analysis	2 days	Thu 5/11/06	Fri 5/12/06		Instructional Designer 2,Ins							
6	Conduct task analysis	2 days	Mon 5/8/06	Tue 5/9/06		Instructional Designer 2[75%							
7	Plan Content	4 days	Mon 5/15/06	Thu 5/18/06	2								
8	Content Planning Meeting	1 day	Mon 5/15/06	Mon 5/15/06		Admin Asst.[11%],Instructio							
9	Design instructional strategies	1 day	Mon 5/15/06	Mon 5/15/06		Instructional Designer 1,Ins							
10	Plan Content and delivery of Instructio	2 days	Wed 5/17/06	Thu 5/18/06	4SS	Instructional Designer 2,Ins							
11	Training Set-Up and Awareness Activitie	2 days	Mon 5/22/06	Tue 5/23/06									
12	Arrange presentation equipment	1 day	Tue 5/23/06	Tue 5/23/06	15SS	Project Manager[33%],Adm							
13	Prepare Awareness Activities	1 day	Mon 5/22/06	Mon 5/22/06		Instructional Designer 2[50%							
14	Distribute awareness activities	1 day	Tue 5/23/06	Tue 5/23/06		Admin Asst.							
15	Develop 1st draft products	8 days	Mon 5/22/06	Wed 5/31/06									
16	Develop instructor guide	2.5 days	Mon 5/22/06	Wed 5/24/06									
17	Front-end material	1 day	Mon 5/22/06	Mon 5/22/06		Instructional Designer 2,Grā							
18	Presentation guidance	1 day	Tue 5/23/06	Tue 5/23/06	17	Instructional Designer 2,Grā							
19	Reference section	0.5 days	Wed 5/24/06	Wed 5/24/06	18	Instructional Designer 2,Wri							
20	Develop student guide	7 days	Tue 5/23/06	Wed 5/31/06									
21	Front-end material	1 day	Tue 5/23/06	Tue 5/23/06		Instructional Designer 2[33%							
22	Lesson guidance	1 day	Wed 5/24/06	Wed 5/24/06	21	Instructional Designer 2[33%							
23	Printed student instructional mate	1 day	Thu 5/25/06	Thu 5/25/06	22	Instructional Designer 2							
24	Instructional materials	1 day	Fri 5/26/06	Fri 5/26/06	23	Instructional Designer 2							
25	Develop Test Items	2 days	Mon 5/29/06	Tue 5/30/06	24	Test Developer							
26	Evaluation materials	1 day	Wed 5/31/06	Wed 5/31/06	25	Instructional Designer 2[25%							
27	Develop PowerPoint & Job Aide	2 days	Wed 5/24/06	Thu 5/25/06		Graphic Artist,Instructional I							
28	Conduct formative evaluation	1 day	Tue 5/30/06	Tue 5/30/06		Instructional Designer 1[3							
29	Revise materials/Complete final draft	3 days	Wed 5/31/06	Fri 6/2/06									
30	Revise materials	2 days	Wed 5/31/06	Thu 6/1/06		Instructional Designer 1[25%							




Project: SWEBC-4.1mpp Date: Tue 11/27/07	Task		Rolled Up Task		External Tasks	
	Progress		Rolled Up Milestone		Project Summary	
	Milestone		Rolled Up Progress		Group By Summary	
	Summary		Split		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	May 7, '06						
							S	M	T	W	T	F	S
31	Print materials	1 day	Fri 6/2/06	Fri 6/2/06	30	Admin Asst.							
32	Conduct Workshop	1 day	Mon 6/5/06	Mon 6/5/06	31	Trainer							
33	Evaluate Workshop	0.25 days	Tue 6/6/06	Tue 6/6/06	32	SW EBC Managers							
34	Conduct summative evaluation	5 days	Mon 7/10/06	Fri 7/14/06	33								
35	Evaluate transfer of skills & knowledge	2 days	Mon 7/10/06	Tue 7/11/06		Evaluation Specialist[50%],							
36	Evaluate impact on performance	1 day	Wed 7/12/06	Wed 7/12/06	35	Evaluation Specialist[50%],							
37	Write report	2 days	Thu 7/13/06	Fri 7/14/06	36	Writer							


Project: SWEBC-4.1mpp Date: Tue 11/27/07	Task		Rolled Up Task		External Tasks	
	Progress		Rolled Up Milestone		Project Summary	
	Milestone		Rolled Up Progress		Group By Summary	
	Summary		Split		Deadline	

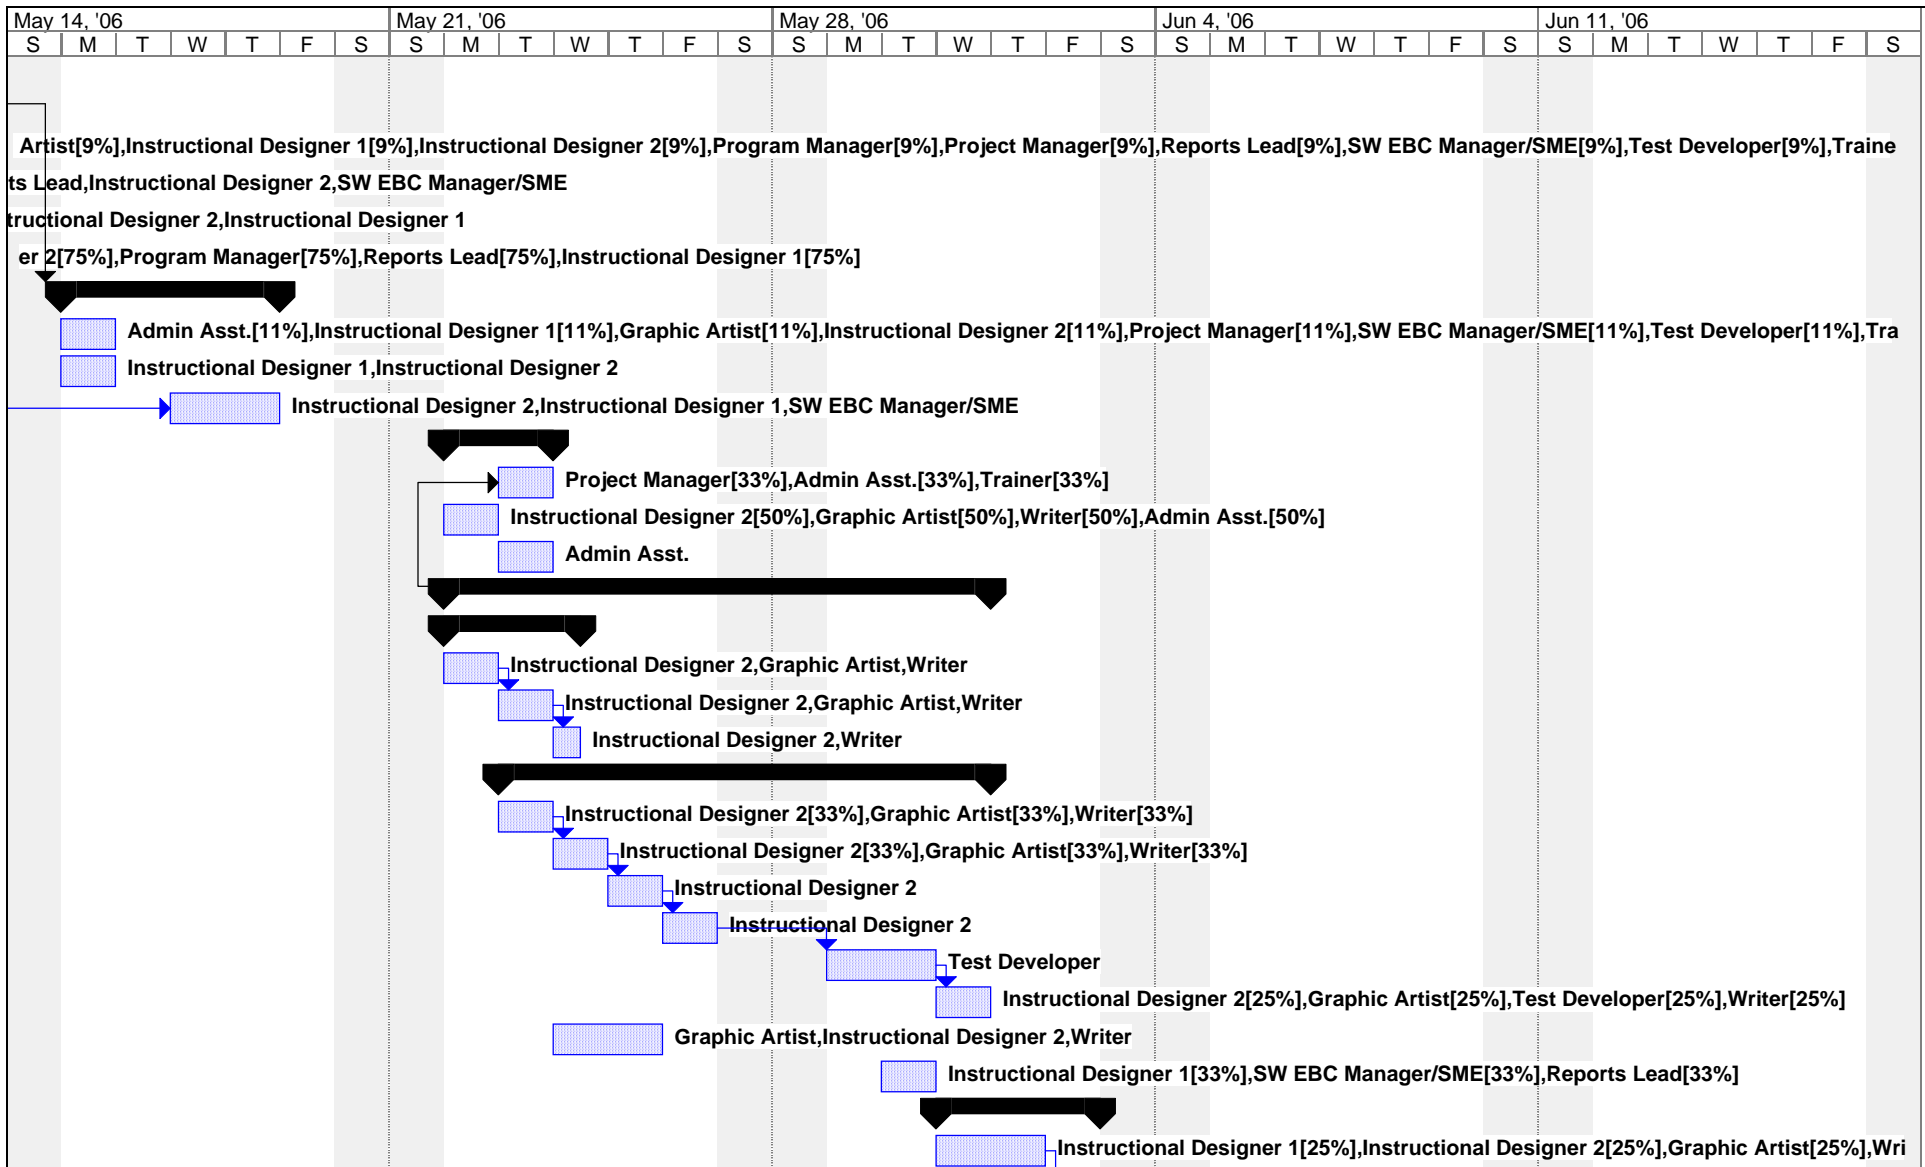


Project: SWEBC-4.1mpp Date: Tue 11/27/07	Task		Rolled Up Task		External Tasks	
	Progress		Rolled Up Milestone		Project Summary	
	Milestone		Rolled Up Progress		Group By Summary	
	Summary		Split		Deadline	

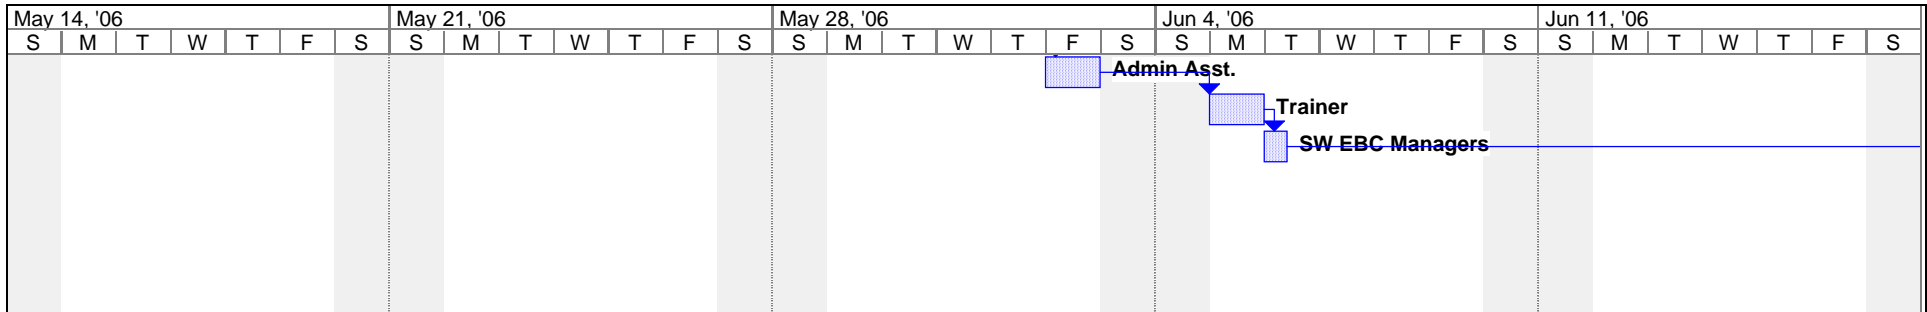



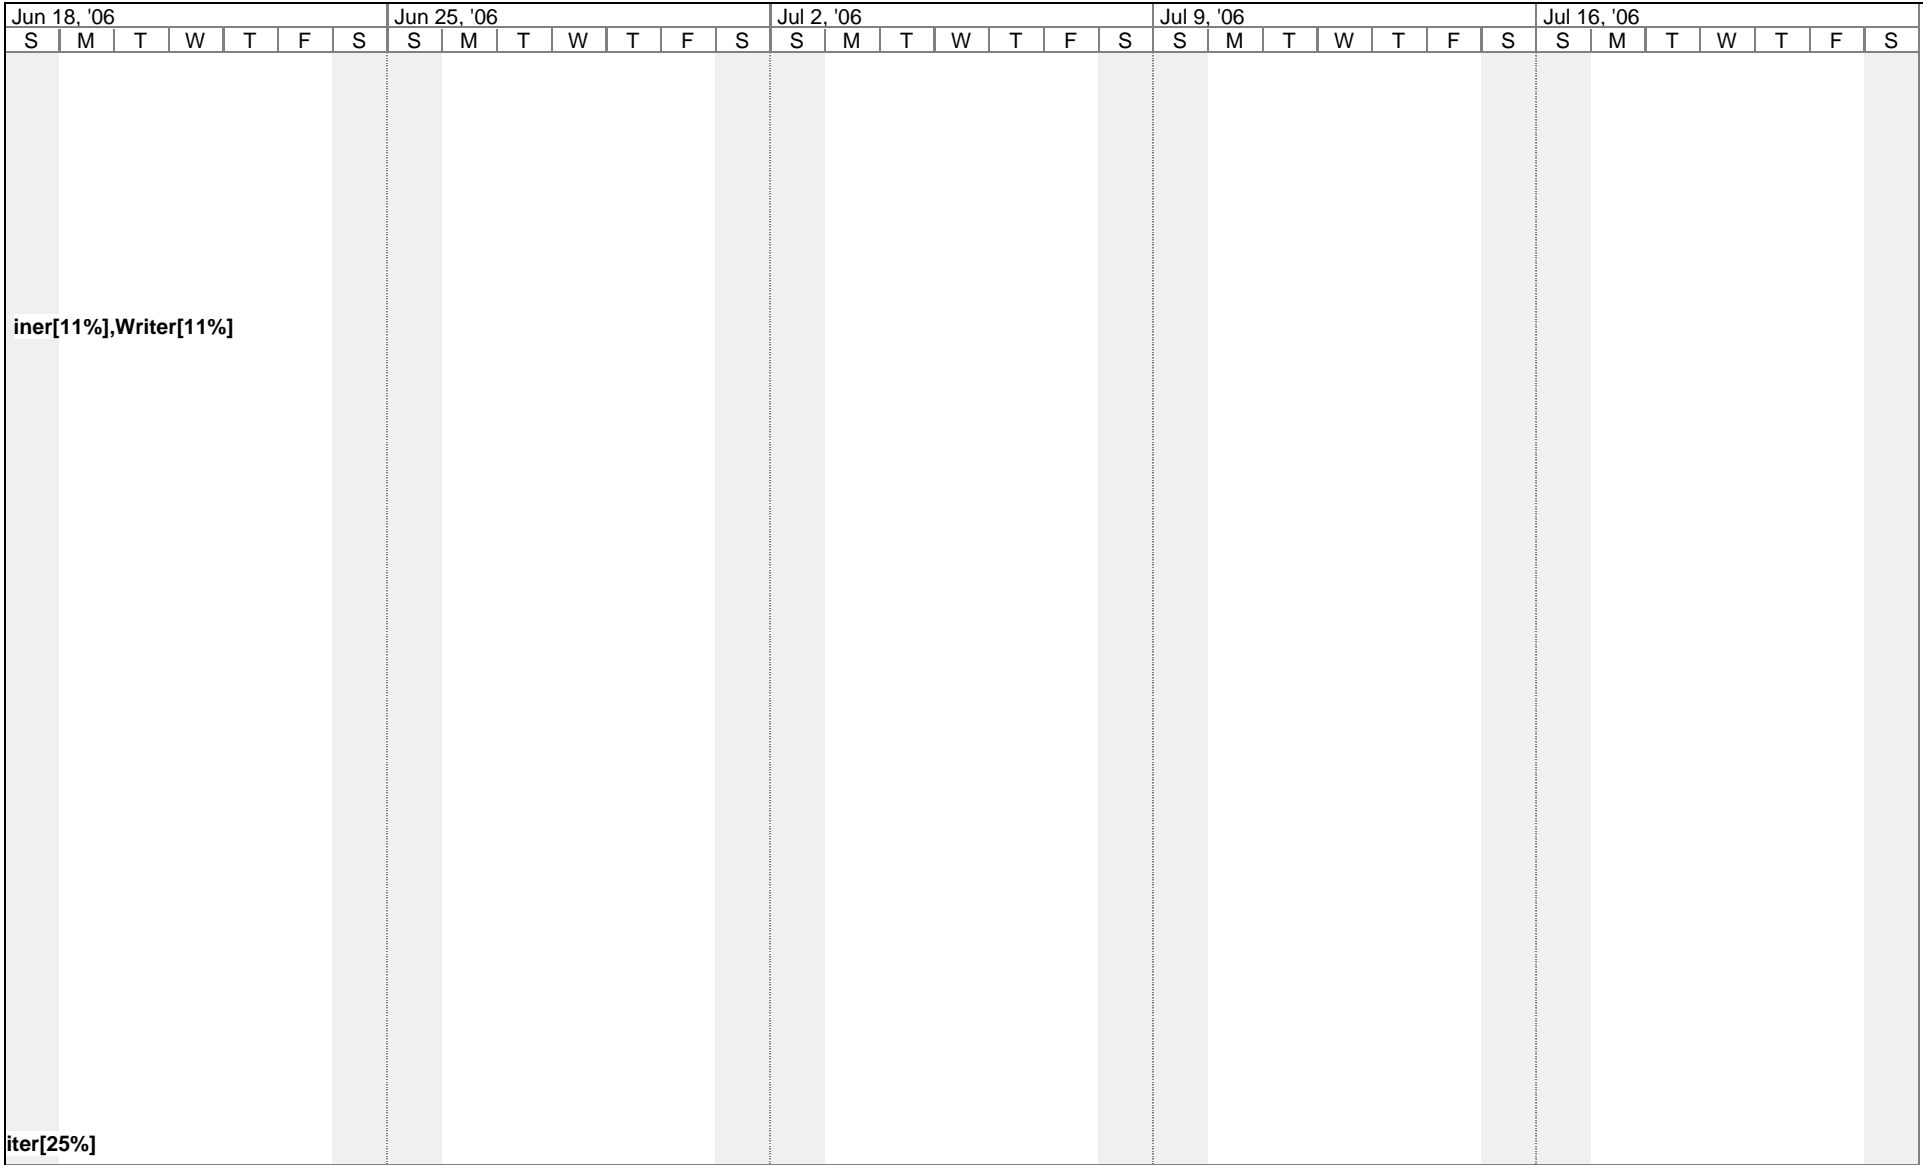



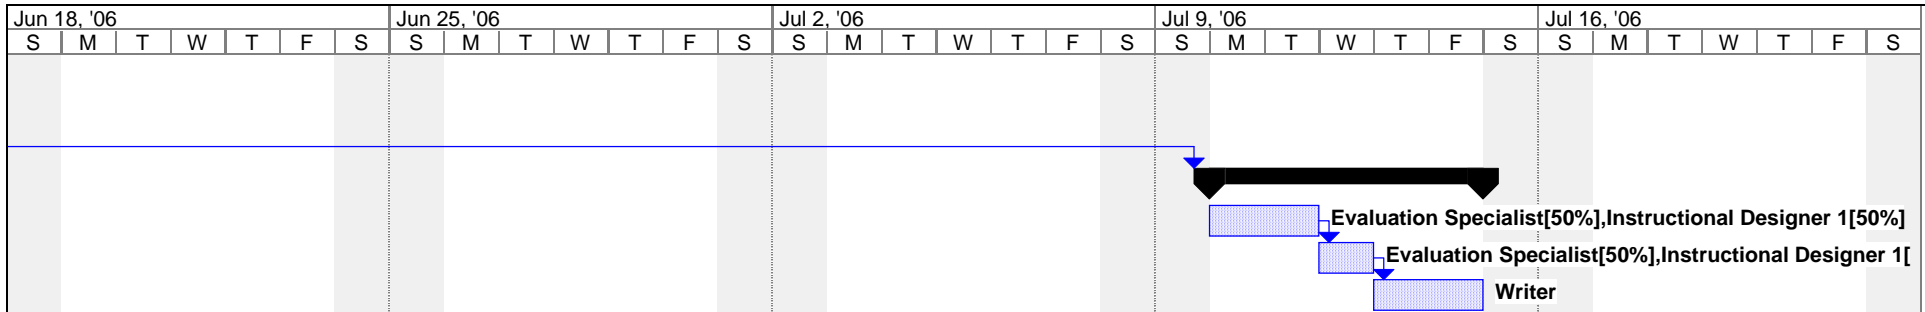




Project: SWEBC-4.1mpp Date: Tue 11/27/07	Task		Rolled Up Task		External Tasks	
	Progress		Rolled Up Milestone		Project Summary	
	Milestone		Rolled Up Progress		Group By Summary	
	Summary		Split		Deadline	



Project: SWEBC-4.1mpp Date: Tue 11/27/07	Task		Rolled Up Task		External Tasks	
	Progress		Rolled Up Milestone		Project Summary	
	Milestone		Rolled Up Progress		Group By Summary	
	Summary		Split		Deadline	



Project: SWEBC-4.1mpp Date: Tue 11/27/07	Task 	Rolled Up Task 	External Tasks 
	Progress 	Rolled Up Milestone 	Project Summary 
	Milestone 	Rolled Up Progress 	Group By Summary 
	Summary 	Split 	Deadline 
